



2023 NATHAN LANE AREA PAVEMENT REHABILITATION NEWSLETTER



Project
Schedule



Project
Contacts



Phasing
Map



PROJECT SCHEDULE

A construction schedule has been provided by the city's contractor, Park Construction Company. A phasing map and anticipated construction schedule is provided on the last page of this newsletter. The schedule provided is an estimate and may change based on weather or other factors. The following is an overview of the upcoming project schedule.

Week of September 4th

- No work on Monday, September 4th due to the Labor Day holiday.
- The first layer of asphalt will be paved in areas that have been reclaimed (gravel roads).
- Utility work will be completed in Phase 2.
- Work to build the realigned intersection at 56th Avenue and Nathan Lane will continue.

Later in September

- All concrete work will be completed in Phase 2.
- Street sections with existing pavement will be reclaimed (ground up) and the first layer of asphalt will be paved.
- The first layer of asphalt will be paved at the realigned intersection of 56th Avenue and Nathan Lane.

October

- Turf restoration will be completed in Phase 2.
- The final layer of asphalt will be paved throughout all of Phase 2.
- Permanent street signs and pavement markings will be installed throughout the project area.
- Final clean-up and punch list work will occur.



PROJECT CONTACTS

Project Help Line (763)-331-8619

Arianna Christian, of Bolton & Menk, Inc. is the Construction Observer for the project. She will be on-site daily and is one of the primary contacts for residents and business during construction. She can be reached at (612) 398-8949 or arianna.christian@bolton-menk.com


Nick Amatuccio, of Bolton & Menk, Inc., is the Project Manager overseeing the construction process and will serve as another contact. He can be reached at (612)-965-3926 or nickam@bolton-menk.com

Tony Miller is the Engineering Project Manager for the City of Plymouth and will be the main contact at the city for this project. He can be reached at (763) 509-5528 or tmmiller@plymouthmn.gov

Website: The project page on the city website will be updated approximately weekly with the latest project info once construction starts. Residents can sign up for email updates at plymouthmn.gov/nathanarea



PROJECT PHASING MAP

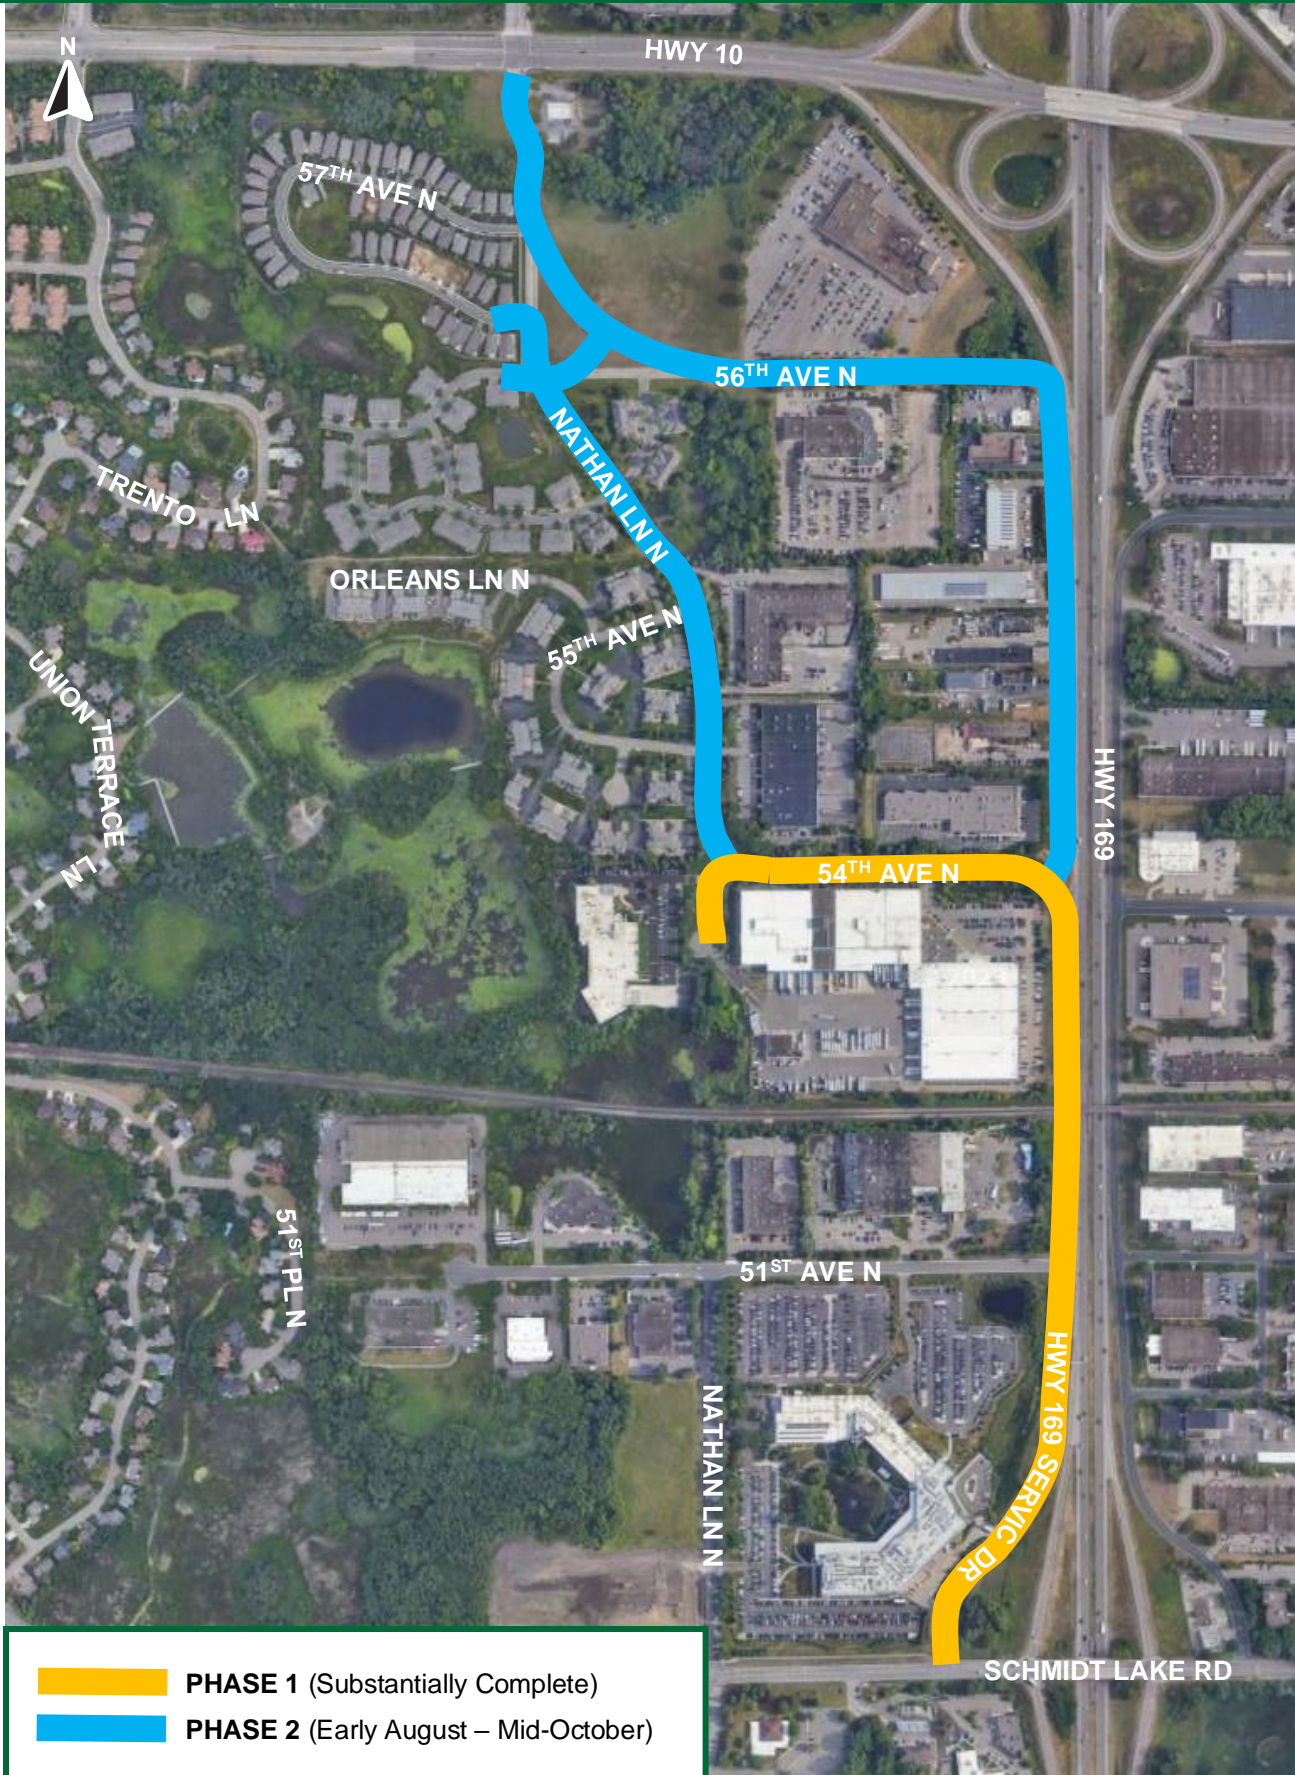

PHASE 1 (Substantially Complete)



PHASE 2 (Early August – Mid-October)
